

Trent Newport - CrossRoad Engineers 980-1555

* Contacts for water main relocation



Scott Purdue
Superintendent

Bryan McHugh
Project Manager

Emily Lucas



The Hunt Paving Company, Inc.

2450 South Tibbs Avenue
Post Office Box 42517
Indianapolis, Indiana 46242-0517
Office: 317-241-8313
Fax: 317-487-5779
Cell: 317-710-4253

Hunt Construction Group, Inc.
2450 South Tibbs Avenue
Indianapolis, Indiana 46241

Hunt Construction Group, Inc.
2450 South Tibbs Avenue (46241)
Post Office Box 128
Indianapolis, Indiana 46206-0128

Mobile: (317) 289-2970
Phone: (317) 227-7800
Fax: (317) 227-7830

Phone: (317) 227-7800
Mobile: (317) 331-5941
Fax: (317) 487-5779

E-mail:
bmcHugh@huntconstructiongroup.com

emlucas@huntconstructiongroup.com



Bryan Gessner
Director of Site Development

8162 Duke Boulevard
Mason, OH 45040
Corporate: 513-679-6800
Cell: 513-617-1222
Fax: 513-679-6803

Randy Eckhart
Site Superintendent

8162 Duke Boulevard
Mason, OH 45040
Corporate: 513-679-6800
Cell: 513-200-9335
Fax: 513-679-6803


MBE
OH LIC# 25648

Director of Site Development
www.tritonservicesinc.com

MBE
OH LIC# 25648

Site Superintendent
www.tritonservicesinc.com

Start date

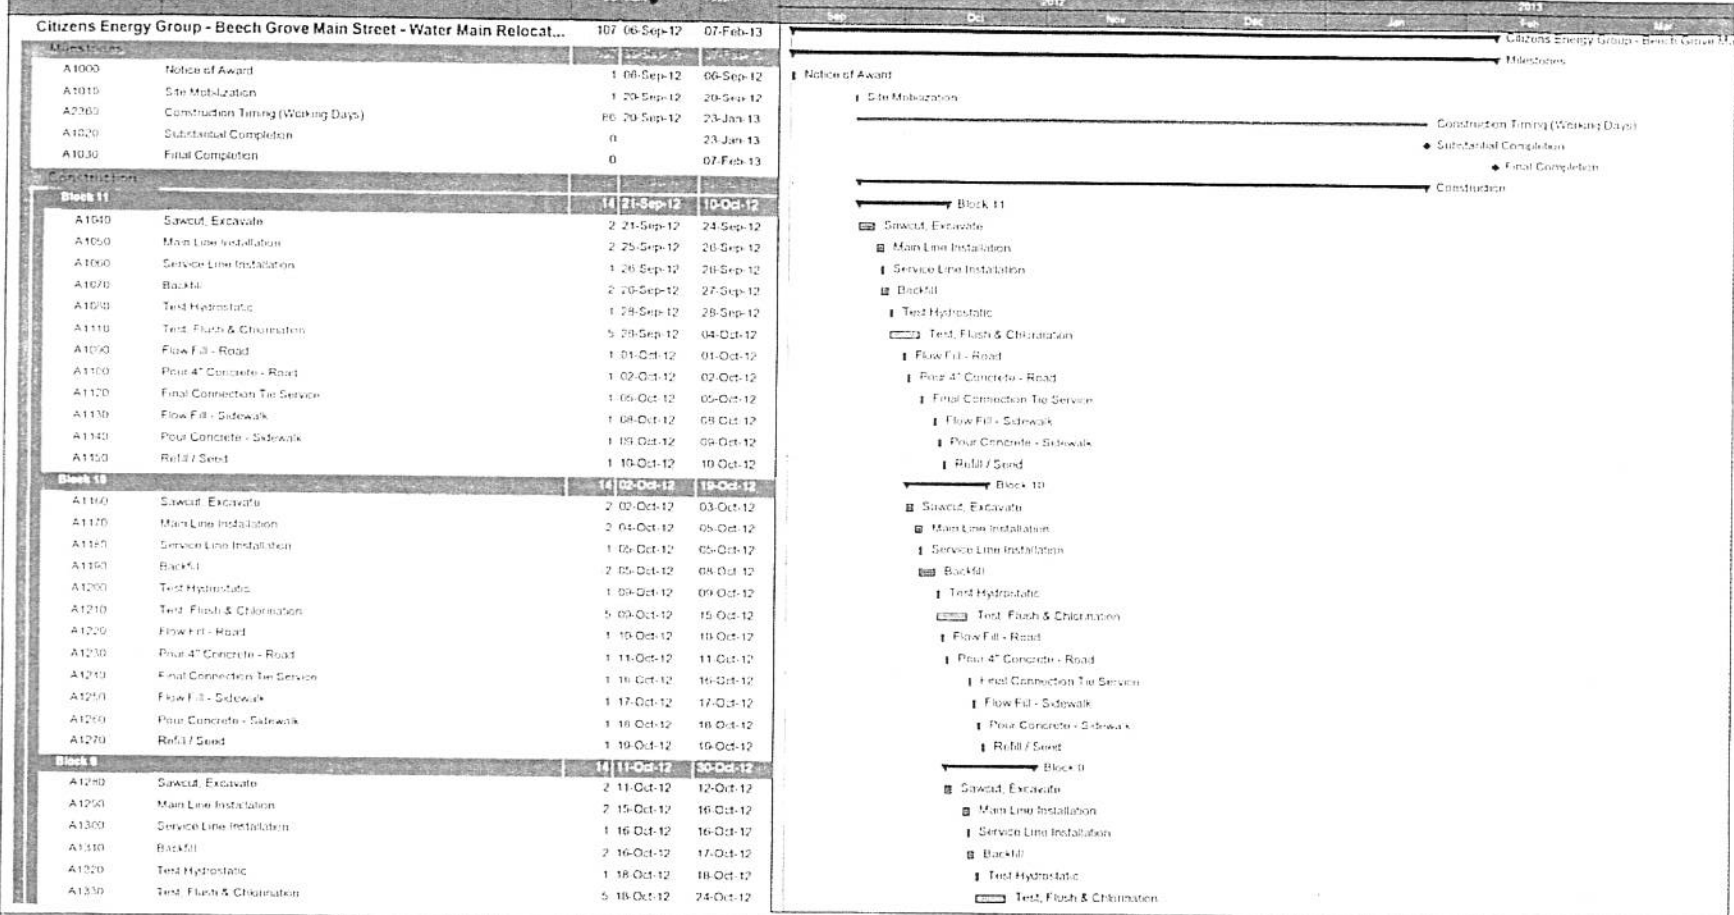

11th St.

10th St.

9th St.

— Remaining Level of Effort ◆ Milestone
 — Actual Level of Effort ← Summary
 — Actual Work
 — Remaining Work
 — Critical Remaining Work



Start date



Project: Citizens Energy Group - Beech Grove Main Street - Water Main Relocation			Layout: ceg - beech grove			Date: 10-Sep-12 Time: 09:20		
Activity ID	Activity Name	CO Start	Finish	2012	2013	2014	2015	2016
A1340	Flow Fill - Road	1 19-Oct-12	19-Oct-12					
A1350	Pour 4" Concrete - Road	1 22-Oct-12	22-Oct-12					
A1360	Final Connection Tie Service	1 25-Oct-12	25-Oct-12					
A1370	Flow Fill - Sidewalk	1 26-Oct-12	26-Oct-12					
A1380	Pour Concrete - Sidewalk	1 29-Oct-12	29-Oct-12					
A1390	Refill / Seed	1 30-Oct-12	30-Oct-12					
Block 6		14 22-Oct-12	05-Nov-12					
A1400	Sawcut, Excavate	2 22-Oct-12	23-Oct-12					
A1410	Main Line Installation	2 24-Oct-12	25-Oct-12					
A1420	Service Line Installation	1 25-Oct-12	25-Oct-12					
A1430	Backfill	2 25-Oct-12	26-Oct-12					
A1440	Test Hydrostatic	1 29-Oct-12	29-Oct-12					
A1450	Test, Flush & Chlorination	5 29-Oct-12	02-Nov-12					
A1460	Flow Fill - Road	1 30-Oct-12	30-Oct-12					
A1470	Pour 4" Concrete - Road	1 31-Oct-12	31-Oct-12					
A1480	Final Connection Tie Service	1 05-Nov-12	05-Nov-12					
A1490	Flow Fill - Sidewalk	1 06-Nov-12	06-Nov-12					
A1500	Pour Concrete - Sidewalk	1 07-Nov-12	07-Nov-12					
A1510	Refill / Seed	1 08-Nov-12	08-Nov-12					
Block 7		14 31-Oct-12	10-Nov-12					
A1520	Sawcut, Excavate	2 31-Oct-12	01-Nov-12					
A1530	Main Line Installation	2 02-Nov-12	05-Nov-12					
A1540	Service Line Installation	1 05-Nov-12	05-Nov-12					
A1550	Backfill	2 05-Nov-12	06-Nov-12					
A1560	Test Hydrostatic	1 07-Nov-12	07-Nov-12					
A1570	Test, Flush & Chlorination	5 07-Nov-12	13-Nov-12					
A1580	Flow Fill - Road	1 08-Nov-12	08-Nov-12					
A1590	Pour 4" Concrete - Road	1 09-Nov-12	09-Nov-12					
A1600	Final Connection Tie Service	1 14-Nov-12	14-Nov-12					
A1610	Flow Fill - Sidewalk	1 15-Nov-12	15-Nov-12					
A1620	Pour Concrete - Sidewalk	1 16-Nov-12	16-Nov-12					
A1630	Refill / Seed	1 19-Nov-12	19-Nov-12					
Block 8		14 09-Nov-12	30-Nov-12					
A1640	Sawcut, Excavate	2 09-Nov-12	12-Nov-12					
A1650	Main Line Installation	2 13-Nov-12	14-Nov-12					
A1660	Service Line Installation	1 14-Nov-12	14-Nov-12					
A1670	Backfill	2 14-Nov-12	15-Nov-12					
A1680	Test Hydrostatic	1 16-Nov-12	16-Nov-12					
A1690	Test, Flush & Chlorination	5 16-Nov-12	26-Nov-12					
A1700	Flow Fill - Road	1 19-Nov-12	19-Nov-12					
A1710	Pour 4" Concrete - Road	1 20-Nov-12	20-Nov-12					

8th St.

7th St.

6th St.



Remaining Level of Effort Milestone
 Actual Level of Effort Summary
 Actual Work
 Remaining Work
 Critical Remaining Work

Hunt Construction Group - Project No. 43815
 Citizens Energy Group
 Beech Grove Main Street - Water Main Relocation
 Data Date: 10-Sep-12



Start date



Project: Citizens Energy Group - Beech Grove Main Street - Water Main Relocation			Layout: ceg - beech grove			Date: 10-Sep-12 Time: 09:07		
Activity ID	Activity Name	Start	Finish	2012	2012	2012	2012	2012
A1720	Final Connection Tie Service	1 27-Nov-12	27-Nov-12					
A1730	Flow Fill - Sidewalk	1 28-Nov-12	28-Nov-12					
A1740	Pour Concrete - Sidewalk	1 29-Nov-12	29-Nov-12					
A1750	Refill / Seed	1 30-Nov-12	30-Nov-12					
Block 6		14 00-Nov-12	11-Dec-12					
A1760	Sawcut, Excavate	2 20-Nov-12	21-Nov-12					
A1770	Main Line Installation	2 26-Nov-12	27-Nov-12					
A1780	Service Line Installation	1 27-Nov-12	27-Nov-12					
A1790	Backfill	2 27-Nov-12	28-Nov-12					
A1800	Test Hydrostatic	1 28-Nov-12	29-Nov-12					
A1810	Test, Flush & Chlorination	5 28-Nov-12	05-Dec-12					
A1820	Flow Fill - Road	1 30-Nov-12	30-Nov-12					
A1830	Pour 4" Concrete - Road	1 03-Dec-12	03-Dec-12					
A1840	Final Connection Tie Service	1 05-Dec-12	06-Dec-12					
A1850	Flow Fill - Sidewalk	1 07-Dec-12	07-Dec-12					
A1860	Pour Concrete - Sidewalk	1 10-Dec-12	10-Dec-12					
A1870	Refill / Seed	1 11-Dec-12	11-Dec-12					
Block 4		14 03-Dec-12	20-Dec-12					
A1880	Sawcut, Excavate	2 03-Dec-12	04-Dec-12					
A1890	Main Line Installation	2 05-Dec-12	06-Dec-12					
A1900	Service Line Installation	1 06-Dec-12	06-Dec-12					
A1910	Backfill	2 06-Dec-12	07-Dec-12					
A1920	Test Hydrostatic	1 10-Dec-12	10-Dec-12					
A1930	Test, Flush & Chlorination	5 10-Dec-12	14-Dec-12					
A1940	Flow Fill - Road	1 11-Dec-12	11-Dec-12					
A1950	Pour 4" Concrete - Road	1 12-Dec-12	12-Dec-12					
A1960	Final Connection Tie Service	1 17-Dec-12	17-Dec-12					
A1970	Flow Fill - Sidewalk	1 18-Dec-12	18-Dec-12					
A1980	Pour Concrete - Sidewalk	1 19-Dec-12	19-Dec-12					
A1990	Refill / Seed	1 20-Dec-12	20-Dec-12					
Block 3		14 12-Dec-12	05-Jan-13					
A2000	Sawcut, Excavate	2 12-Dec-12	13-Dec-12					
A2010	Main Line Installation	2 14-Dec-12	17-Dec-12					
A2020	Service Line Installation	1 17-Dec-12	17-Dec-12					
A2030	Backfill	2 17-Dec-12	18-Dec-12					
A2040	Test Hydrostatic	1 19-Dec-12	19-Dec-12					
A2050	Test, Flush & Chlorination	5 19-Dec-12	26-Dec-12					
A2060	Flow Fill - Road	1 20-Dec-12	20-Dec-12					
A2070	Pour 4" Concrete - Road	1 21-Dec-12	21-Dec-12					
A2080	Final Connection Tie Service	1 27-Dec-12	27-Dec-12					
A2090	Flow Fill - Sidewalk	1 28-Dec-12	28-Dec-12					

5th St.

4th St.

3rd St.



— Remaining Level of Effort ◆ Milestone
 — Actual Level of Effort ← Summary
 — Actual Work
 — Remaining Work
 — Critical Remaining Work

Hunt Construction Group - Project No. 43815
Citizens Energy Group
Beech Grove Main Street - Water Main Relocation
 Data Date: 06-Sep-12



Start date

2nd St

1st St

Project: Citizens Energy Group - Beech Grove Main Street - Water Main Relocation			Layout: ceg - beech grove				Date: 10-Sep-12 Time: 09:01
Activity ID	Activity Name	OO Start	Finish	2012	2012	2012	
A2100	Pour Concrete - Sidewalk	1-31-Dec-12	31-Dec-12				
A2110	Refrill Sewer	1-02-Jan-13	02-Jan-13				
Block 1		14-27-Dec-12	17-Jan-13				
A2120	Sawcut, Excavate	2-23-Dec-12	24-Dec-12				
A2130	Main Line Installation	2-26-Dec-12	27-Dec-12				
A2140	Service Line Installation	1-27-Dec-12	27-Dec-12				
A2150	Backfill	2-27-Dec-12	28-Dec-12				
A2160	Test Hydrostatic	1-31-Dec-12	31-Dec-12				
A2170	Test, Flush & Commission	5-31-Dec-12	07-Jan-13				
A2180	Flow Fill - Road	1-02-Jan-13	02-Jan-13				
A2190	Pour 4" Concrete - Road	1-03-Jan-13	03-Jan-13				
A2200	Final Connection To Sewer	1-05-Jan-13	05-Jan-13				
A2210	Flow Fill - Sidewalk	1-09-Jan-13	09-Jan-13				
A2220	Pour Concrete - Sidewalk	1-10-Jan-13	10-Jan-13				
A2230	Refrill Sewer	1-11-Jan-13	11-Jan-13				
Block 2		15-02-Jan-13	23-Jan-13				
A2240	Sawcut, Excavate	2-03-Jan-13	04-Jan-13				
A2250	Main Line Installation	2-07-Jan-13	08-Jan-13				
A2260	Service Line Installation	1-09-Jan-13	09-Jan-13				
A2270	Backfill	2-09-Jan-13	10-Jan-13				
A2280	Test Hydrostatic	1-11-Jan-13	11-Jan-13				
A2290	Test, Flush & Commission	5-11-Jan-13	17-Jan-13				
A2300	Flow Fill - Road	1-14-Jan-13	14-Jan-13				
A2310	Pour 4" Concrete - Road	1-15-Jan-13	15-Jan-13				
A2320	Final Connection To Sewer	1-18-Jan-13	18-Jan-13				
A2330	Flow Fill - Sidewalk	1-21-Jan-13	21-Jan-13				
A2340	Pour Concrete - Sidewalk	1-22-Jan-13	22-Jan-13				
A2350	Refrill Sewer	1-23-Jan-13	23-Jan-13				



Remaining Level Effort
 Actual Level Effort
 Actual Work
 Remaining Work
 Critical Remaining Work

Hunt Construction Group - Project No. 43815
Citizens Energy Group
Beech Grove Main Street - Water Main Relocation
 Data Date: 06-Sep-12

