

WEEKLY REPORT OF CONSTRUCTION ACTIVITES



Project Name: Beech Grove Greenway Trail
For Week Ending: 7/24/2021
Date of Notice to Proceed: 10/5/2020
Work Days Previously Reported: 93
Contractor: Morphey Construction
Owner: City of Beech Grove

Report No.: 27
Calendar Completion Date: 11/15/2022
This Report: 3 **Total to Date:** 97
Contract Amount: \$ 3,429,000.00
Paid To Date: \$ 649,926.61
Designer: Crossroad Engineers

Contract Number: R-39660
Project Number: 1600657
Structure Number: _____
Balance Remaining: \$ 2,779,073.39
Project Complete Percent: 19%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 7/18/21	No Work Today	Pedestrian Trail Subgrade	Contractor not on-site	0/24	0
Mon 7/19/21	Morphey was on-site today.	Pedestrian Trail Subgrade	Contractor not on-site	12/24	1
Tues 7/20/21	Morphey was on-site today.	Pedestrian Trail Subgrade	Contractor on-site	12/24	1
Wed 7/21/21	Morphey was on-site today.	Pedestrian Trail Subgrade	Contractor on-site	12/24	1
Thurs 7/22/21	Morphey was on-site today.	Pedestrian Trail Subgrade	Contractor on-site	12/24	1
Fri 7/23/21	Morphey was not on-site today.	Pedestrian Trail Subgrade	Contractor not on-site	12/24	0
Sat 7/24/21	Morphey was not on-site today.	Pedestrian Trail Subgrade	Contractor not on-site	12/24	0

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Morphey spent the week assembling and setting bridge 3

Morphey is planning to assemble Bridge 4 and set it on Thursday the 29th and continue to work on drying the and placing aggregate on the trail.

Prepared by:

Jay Niederhauser
 Project Supervisor - United Consulting

Approved _____ 24-Jul 2021


Jay Niederhauser
 Construction Manager

CONTRACTOR ACCEPTANCE

Jason Umlauf

Project Manager - Morphey Construction

PROJECT PHOTOS

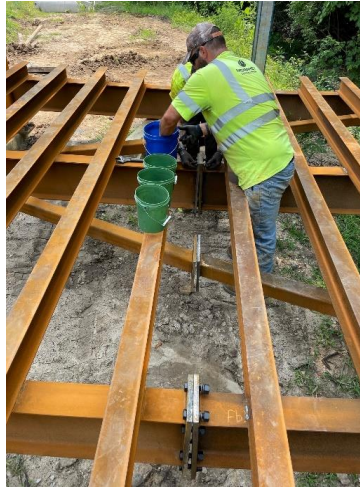


Bridge 3 assembly



Bridge 3 assembly



Bridge 3 assembly

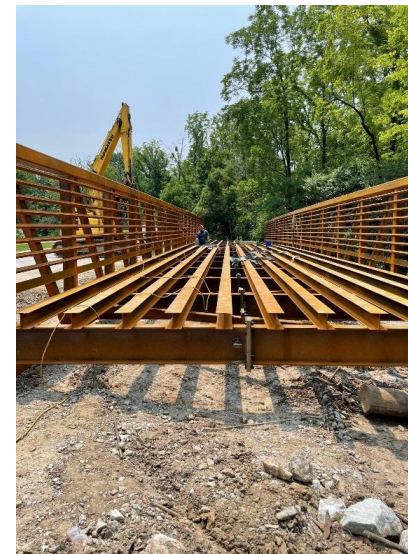

Bridge 3 assembly

PROJECT PHOTOS



Lifting Bridge 3



Rotating Bridge 3



Lifting Bridge 3



Setting Bridge 3
