2014 PAVING SCHEDULE

ID	Task Mode	Task Name	Duration	Start	Finish
1		**BEECH GROVE ROADWAY RESURFACING**	**60 days**	**Tue 8/12/14**	**Sat 10/11/14**
2		Notice to Proceed	1 day	Tue 8/12/14	Tue 8/12/14
18		**Alley / 18th Avenue**	**8 days**	**Mon 8/25/14**	**Wed 9/3/14**
19		Concrete Removals	3 days	Mon 8/25/14	Wed 8/27/14
20		Concrete Work	2 days	Thu 8/28/14	Fri 8/29/14
21		Base Repair	1 day	Sat 8/30/14	Sat 8/30/14
22		Mill	1 day	Tue 9/2/14	Tue 9/2/14
23		Asphalt & Speed Humps	1 day	Wed 9/3/14	Wed 9/3/14
24		**Alley / Churchman**	**1 day**	**Wed 9/3/14**	**Wed 9/3/14**
25		Speed Humps	1 day	Wed 9/3/14	Wed 9/3/14
26		Signs	1 day	Wed 9/3/14	Wed 9/3/14
8		**Buffalo (17th to 18th)**	**7 days**	**Thu 9/4/14**	**Thu 9/11/14**
9		Concrete Removals / Subgrade Treatment	1 day	Thu 9/4/14	Thu 9/4/14
10		Inlet & 12" storm pipe	1 day	Fri 9/5/14	Fri 9/5/14
11		Concrete Work (Alley, Ramps, Drives)	3 days	Sat 9/6/14	Tue 9/9/14
12		Base Repair	1 day	Wed 9/10/14	Wed 9/10/14
13		Mill & Overlay	1 day	Thu 9/11/14	Thu 9/11/14
14		Temporary Striping	1 day	Thu 9/11/14	Thu 9/11/14
15		**Mann Drive**	**2 days**	**Thu 9/11/14**	**Fri 9/12/14**
16		Base Repair	1 day	Thu 9/11/14	Thu 9/11/14
17		Mill & Overlay	1 day	Fri 9/12/14	Fri 9/12/14
27		**Churchman Ave**	**2 days**	**Sat 9/13/14**	**Mon 9/15/14**
28		Concrete Removal'	1 day	Sat 9/13/14	Sat 9/13/14
29		Concrete Work	1 day	Mon 9/15/14	Mon 9/15/14
30		Asphalt Patch	1 day	Mon 9/15/14	Mon 9/15/14
31		**Royal Road**	**15 days**	**Tue 9/16/14**	**Thu 10/2/14**
32		Close Road	1 day	Tue 9/16/14	Tue 9/16/14
33		Silt Fence & Inlet Protection	1 day	Tue 9/16/14	Tue 9/16/14
34		Common Excavation & Haul Off	2 days	Tue 9/16/14	Wed 9/17/14
35		Storm Structures & Pipe & Underdrain	4 days	Thu 9/18/14	Mon 9/22/14
36		Adjust Castings	1 day	Mon 9/22/14	Mon 9/22/14
37		Concrete Approaches	1 day	Tue 9/23/14	Tue 9/23/14
38		Riprap / Grading / Topsoil	1 day	Wed 9/24/14	Wed 9/24/14
39		Subgrade Treatment	2 days	Thu 9/25/14	Fri 9/26/14
40		Asphalt	2 days	Sat 9/27/14	Mon 9/29/14
41		Sod	2 days	Tue 9/30/14	Wed 10/1/14
43		Open Road	1 day	Wed 10/1/14	Wed 10/1/14
42		Temporary Striping	1 day	Thu 10/2/14	Thu 10/2/14
44		**23rd Avenue**	**5 days**	**Sat 9/27/14**	**Thu 10/2/14**
45		Common Excavation	1 day	Sat 9/27/14	Sat 9/27/14
46		Subgrade Treatment / Sidewalk Removal	2 days	Mon 9/29/14	Tue 9/30/14
47		Concrete Ramps	1 day	Wed 10/1/14	Wed 10/1/14
48		Asphalt	1 day	Thu 10/2/14	Thu 10/2/14
3		**8th Avenue (Albany to Buffalo)**	**7 days**	**Fri 10/3/14**	**Fri 10/10/14**
4		Concrete & Pavement Removals	3 days	Fri 10/3/14	Mon 10/6/14
5		Concrete Work (Sidewalks, Ramps, Drives)	2 days	Tue 10/7/14	Wed 10/8/14
6		Type II Subgrade Treatment	1 day	Thu 10/9/14	Thu 10/9/14
7		Asphalt	1 day	Fri 10/10/14	Fri 10/10/14
49		Perm Striping (all areas)	4 days	Wed 10/8/14	Sat 10/11/14
50		Sod (all areas except Royal)	2 days	Thu 10/9/14	Fri 10/10/14

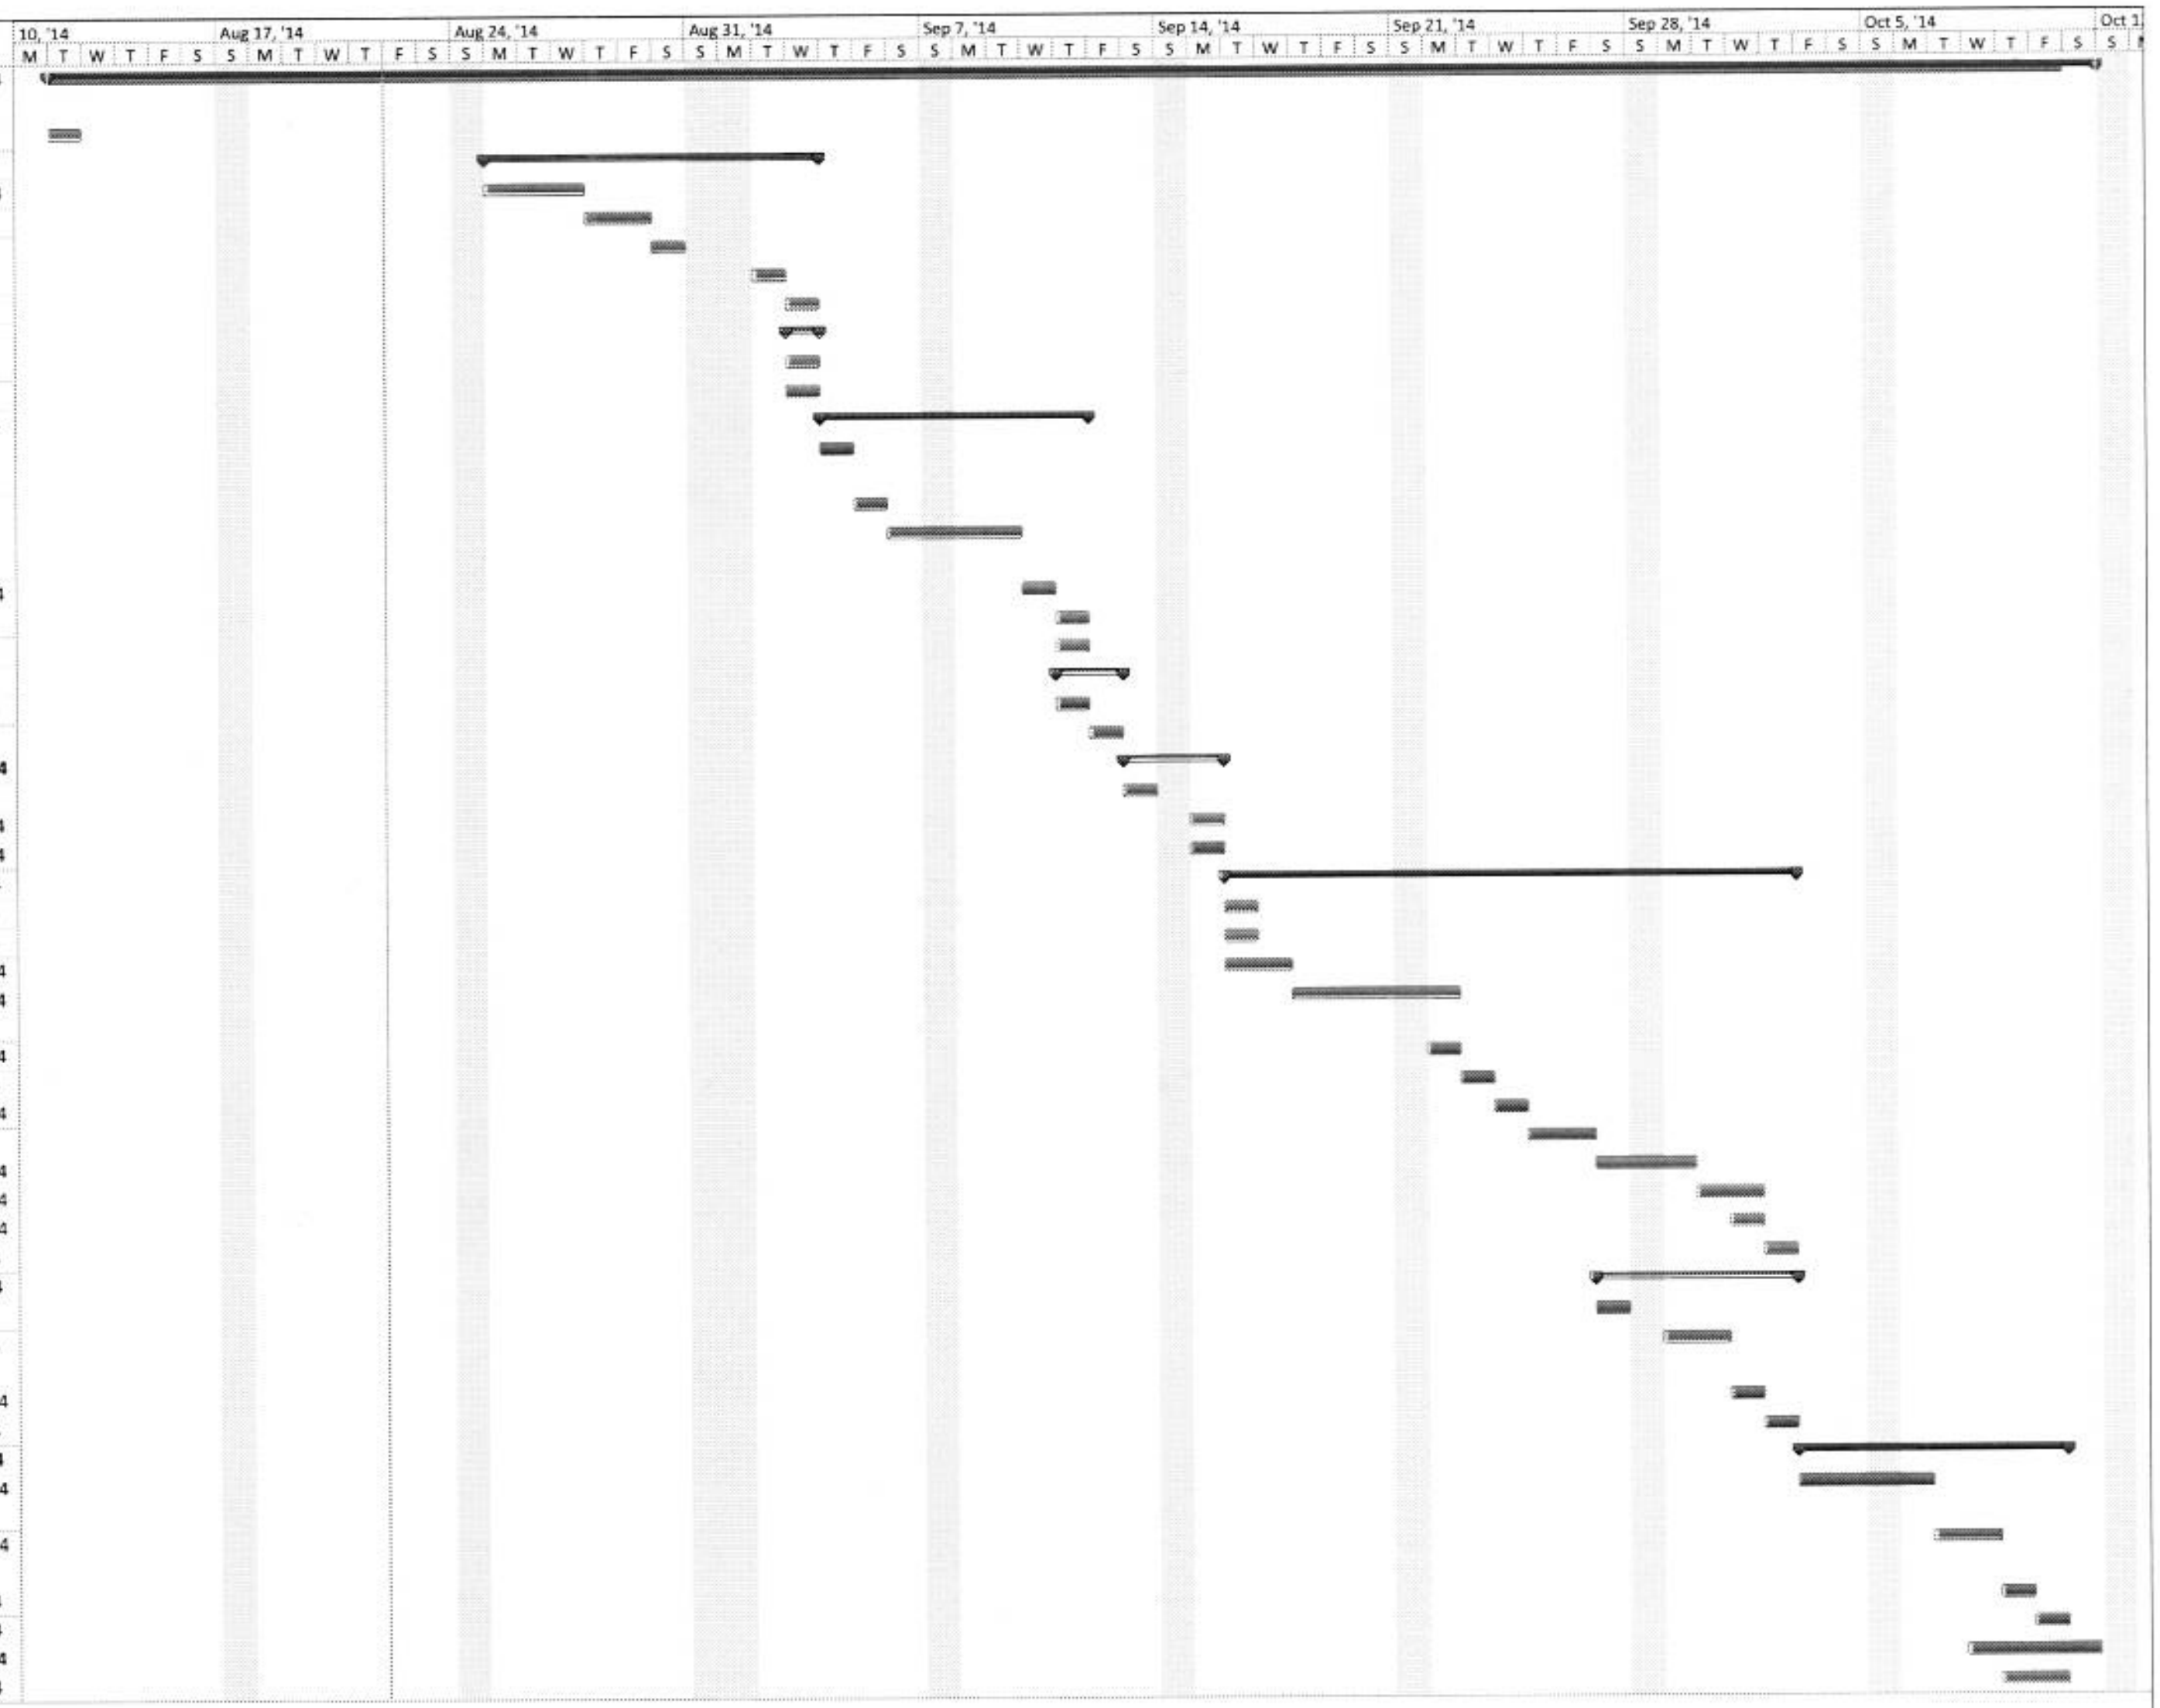

Project: Beech Grove Resurface 8
Date: Fri 8/22/14

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Critical Split	
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline	Progress	
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Critical		
